



CONSTRUCTION PROJECTS REPORT
January 17, 2017
Gloria J. Martinez, Director of Construction

1. LAS CRUCES HIGH SCHOOL ADDITIONS AND RENOVATIONS

Alley & Associates/ASA – Wooten/Sundt

Phase II includes: Building a New Aux Gym, Cafeteria, Tennis & Basketball Courts, and renovating existing classroom spaces, gym etc.

- Finishing up steel work on new cafeteria
- Block work & installation of steel for slab ongoing on new Aux gym
- Block work & interior work ongoing in New Field House
- Framing & interior work continues on the classroom wings
- Construction start date: July 2016
- Estimated completion date: January 2018



Construction Budget	Funding Source
\$ 40,000,000(Phase II)	Bond/PSCOC

**CONSTRUCTION PROJECTS UPDATE
(Continued)**

NEW CAFETERIA FINISHING UP EXTERIOR FRAMING



NEW AUX GYM BLOCK WORK STILL IN PROGRESS



**CONSTRUCTION PROJECTS UPDATE
(Continued)**

NEW AUX GYM BLOCK WORK STILL IN PROGRESS



WORK CONTINUES IN NEW FIELD HOUSE



**CONSTRUCTION PROJECTS UPDATE
(Continued)**

FIELD HOUSE GAMEPLAN ROOM BUILT IN CONCRETE SEATS



EXTERIOR SHEATHING WORK STARTED ON CLASSROOM WINGS



CONSTRUCTION PROJECTS UPDATE
(Continued)

EXTERIOR SHEATING WORK STARTED ON CLASSROOM WINGS



INTERIOR WORK CONTINUES IN CLASSROOM WINGS



CONSTRUCTION PROJECTS UPDATE
(Continued)

2. HERMOSA HEIGHTS ES

Vigil & Associates – ESA

This project will consist of building a new 12,520 sq. ft. multipurpose room, which will include a stage, bleachers, basketball hoops and a new kitchen.

- Site Work includes- New parking lot/delivery area, walkways, grading & drainage
- Alt. #1 includes- Additional parking lot to replace all removed parking
- Alt. #2 Includes- Renovation of existing cafeteria, lobby & entry
- Preconstruction meeting was held Dec 6, 2016.

Project Budget	Funding Source
\$3,500,000.00	Bond



DEMOLITION OF OLD KITCHEN



**CONSTRUCTION PROJECTS UPDATE
(Continued)**

DEMOLITION OF OLD KITCHEN AND PARKING LOT



DEMOLITION COMPLETE/REMOVING DEBREE



CONSTRUCTION PROJECTS UPDATE
(Continued)

3. SIERRA MS RE-ROOF

Jim D. Koontz – ESA

This is a re-roofing project funded by NMPSIA due to hail damage.

- Roof work is ongoing.
- Estimated completion date: January 2017

Project Budget	Funding Source
\$25,000.00 LCPS/ NMPSIA \$1,865,350.29	Capital Outlay Funds/NMPSIA

SIERRA MS RE-ROOFING CONTINUES



4. DESERT HILL ES RE-ROOF

Jim D. Koontz – CD General

This is a re-roofing project funded by NMPSIA due to hail damage.

- Roof work is ongoing.
- Estimated completion date: January 2017

Project Budget	Funding Source
\$25,000.00 LCPS/ NMPSIA \$539,406.90	Capital Outlay Funds/NMPSIA

CONSTRUCTION PROJECTS UPDATE
(Continued)

5. ALMA D'ARTE RE-ROOF

Jim D. Koontz – CD General

This is a re-roofing project funded by NMPSIA due to hail damage.

- Roof work is ongoing.
- Estimated completion date: January 2017

Project Budget	Funding Source
\$25,000.00 LCPS/ NMPSIA \$546,544.88	Capital Outlay Funds/NMPSIA

ALMA D'ARTE RE-ROOFING CONTINUES



CONSTRUCTION PROJECTS UPDATE (Continued)

6. SECURITY FENCING


ASA Architects-ESA

- This project will consist of adding gates to secure entry to each school. These schools are:
 - Lynn Middle School- Completion January 2017
 - CRMS- Completion January 2017

LYNN MIDDLE SCHOOL SECURITY FENCING



LYNN MIDDLE SCHOOL SECURITY FENCING

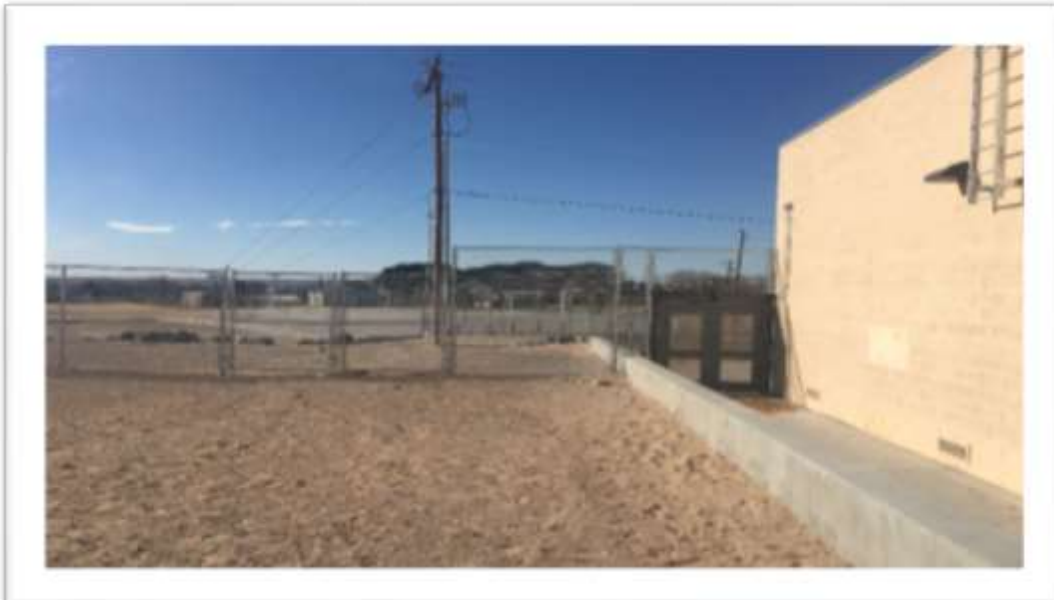

**CONSTRUCTION PROJECTS UPDATE
(Continued)**

LYNN MIDDLE SCHOOL SECURITY FENCING



LYNN MIDDLE SCHOOL SECURITY FENCING



CONSTRUCTION PROJECTS UPDATE
(Continued)

CAMINO MIDDLE SCHOOL SECURITY FENCING



CAMINO MIDDLE SCHOOL SECURITY FENCING



CONSTRUCTION PROJECTS UPDATE
(Continued)

7. JORNADA ES

WDG Architects-ESA Construction

- This is a remodel that will relocate the front office and main entrance into the school.
 - Interior framing work ongoing
 - Exterior block work ongoing

<i>Project Budget</i>	<i>Funding Source</i>
800,000	Bond

STEEL FRAMING ON NEW FRONT ENTRANCE



CONSTRUCTION PROJECTS UPDATE
(Continued)

INTERIOR FRAMING



INTERIOR FRAMING



CONSTRUCTION PROJECTS UPDATE
(Continued)

8. MAYFIELD HIGH SCHOOL CAFETERIA renovation

AKS Architect-

- Architect currently working on the design of the renovation

<i>Project Budget</i>	<i>Funding Source</i>
2,000,000	Bond
